IAS & Last Rev
Q4 2025 Quarterly Review

Prepared by Last Rev for IAS Executive Leadership

Covering October – December 2025

EXECUTIVE SUMMARY

Quarter in Review: Strategic Progress Across Key Initiatives

Q4 2025 marked significant advancement in our AI capabilities, security infrastructure, and user-facing platforms. The quarter demonstrated strong execution across three core workstreams: AnswerAI platform evolution, Help Center and Policy Resource Center enhancements, and enterprise security strengthening.

Our work centered on preparing AnswerAI for external deployment through critical safety guardrails, advancing internal tooling with role-based access controls and workspace management, and streamlining content operations through automation. Security became a first-class citizen in our deployment process, with formalized review gates now standard for all releases.

Key accomplishments include AnswerAI v2.0 development with RBAC and Workspaces, Fiddler Guardrails integration scoping for external chatbot safety, Help Center recertification flow completion, and comprehensive PRC feature delivery. Translation automation architecture was scoped to accelerate multilingual content delivery.

Executive Strategic Alignment sessions in October and November ensured leadership visibility, while contract renewal discussions progressed to secure partnership continuity into 2026. Weekly deployment cadence and BigQuery reporting automation strengthened operational rigor.

ANSWERAI PLATFORM

AnswerAgent Evolution: Building Production-Ready AI

AnswerAgent serves as IAS's AI-powered chatbot platform, supporting both internal users through Chief and Sidekick implementations and customer-facing CS use cases. Q4 focused on maturing the platform toward external deployment readiness while enhancing internal capabilities.

Platform Development

AnswerAI v2.0 development progressed with Role-Based Access Control implementation, Workspaces feature for team collaboration, and performance optimization to handle increased load

Integration Expansion

Segment API integration delivered, enabling AI-powered responses within Signal 2 Custom Segment Editor. External user tracking enhancement scoped for improved analytics capabilities

Quality Assurance

AAI evaluations launched November 21 to measure chatbot accuracy and response quality. Chief chatflow updates conducted with evaluation sessions to refine user experience

Operational Excellence

Weekly deployment sessions maintained consistent cadence. BigQuery automated reporting pipeline established for usage dashboards. OpenAI usage statistics tracked in weekly syncs

AI SAFETY

Fiddler Guardrails: Enabling Responsible External AI

Integration Overview

Scoped October 30 with Fiddler team to implement safety guardrails for customer-facing chatbot deployment

Critical Milestone

This integration represents a foundational requirement for production-ready external AnswerAgent, ensuring responsible AI usage and content filtering

Strategic Importance

As IAS moves toward external chatbot deployment, implementing robust safety measures becomes paramount. Fiddler Guardrails provides enterprise-grade content filtering, bias detection, and output validation to ensure customer interactions meet quality and safety standards.

01

Integration scoping completed

Architecture defined with Fiddler team

02

Implementation plan established

Targeted for external chatbot deployment

03

Production readiness pathway

Critical gate for customer-facing AI

CONTENT PLATFORMS

Help Center & PRC: Enhanced User Experience Delivered

The Help Center and Policy Resource Center serve as critical Contentful-based properties for IAS users, providing self-service documentation and policy resources. Q4 delivered significant feature enhancements and prepared recertification capabilities for launch.

1

Recertification Flow

Code merged and ready for User Acceptance Testing. This workflow enables systematic content review and validation, ensuring documentation accuracy and compliance requirements are met on schedule.

2

PRC Feature Suite

Multiple enhancements delivered: content owner display on articles for accountability, improved sort options for navigation, embedded document indicators, and Google Analytics metrics integration for usage insights.

3

User Feedback System

Thumbs up/down feedback mechanism implemented with comment box for qualitative insights. This data will inform content improvement priorities and measure user satisfaction over time.

4

Access Control Validation

Reseller user access validated to ensure search results are properly scoped to authorized articles only. Conveyor integration scoped November 24 to surface PRC content in expanded contexts.

AUTOMATION

Translation Automation: Accelerating Global Content Delivery

Architecture & Approach

A Contentful webhook-based translation agent architecture was scoped in Q4 to dramatically reduce manual translation effort and improve time-to-publish for multilingual content across international markets.

The automated translation pipeline is designed to trigger on content publish events, creating a seamless workflow where content creators can focus on authoring while the system handles translation orchestration. This initiative addresses a critical bottleneck in Help Center content velocity.

Next Steps

IAS Translation SOW was discussed in December sprint planning. Finalization of the statement of work will enable development to begin in Q1 2026, with expected delivery significantly improving content operations efficiency.

Manual Translation

Current state: time-intensive manual process creating publication delays

Webhook Trigger

Contentful publish events automatically initiate translation workflow

Automated Processing

Translation agent handles content transformation across target languages

Rapid Publication

Multilingual content available to global users with minimal delay

SECURITY & COMPLIANCE

Security Posture: Formalized Controls & Zero-Trust Deployment

Q4 established security as a foundational element of all deployment activities, implementing formal review processes and addressing infrastructure access challenges to ensure robust protection of IAS systems and data.

Release Review Gates

Security QA processes formally established with IAS security team reviewing all releases before deployment. This zero-trust approach ensures no code reaches production without explicit security approval.

Issue Tracking

Security open items tracked and addressed systematically in weekly deployment sessions, ensuring visibility and accountability for remediation timelines and priorities.

Background Verification

Background check coordination completed for team members requiring access to sensitive IAS systems, meeting compliance requirements for personnel security.

Data Access Resolution

Salesforce, Jira, and Confluence data access inconsistencies identified and debugged November 12, resolving potential AnswerAgent data quality issues.

METRICS & ANALYTICS

Tracking Framework: Measuring Performance & Usage

Current Monitoring Capabilities

A comprehensive tracking framework was established in Q4 to provide visibility into platform performance, user engagement, and operational health across all workstreams.

- OpenAI API usage statistics including tokens, requests, and costs reviewed in weekly syncs
- AnswerAgent response quality metrics via AAI evaluations measuring accuracy and helpfulness
- Help Center article engagement through Google Analytics tracking user behavior patterns
- PRC user feedback via thumbs up/down mechanism capturing satisfaction data
- Reseller search authorization accuracy ensuring proper content scoping
- BigQuery automated reporting enabling usage dashboards for stakeholder visibility
- Budget burndown tracked with Susan's team for financial oversight

Recommendation: Executive KPI Dashboard

While individual metrics are being tracked effectively, consolidating these into a formalized KPI dashboard for Q1 2026 executive reporting would provide unified visibility into program health, identify trends earlier, and enable data-driven decision making at the leadership level.

Analytics Infrastructure

The BigQuery automated reporting pipeline represents a significant advancement in operational maturity, moving from manual metric compilation to systematic data collection and visualization. This foundation enables more sophisticated analysis as the platform scales.

RESOURCE MANAGEMENT

Budget & Resource Utilization: Q4 Allocation

Budget and resource management maintained disciplined oversight throughout Q4, balancing investment across AnswerAI platform development, content platform enhancements, and security infrastructure while planning for 2026 continuity.

Financial Tracking

Budget burndown tracking maintained continuously with Susan's team throughout Q4, ensuring spend aligned with projections and no surprises in quarterly reconciliation.

Sprint Planning & Billing

December 8 sprint planning session addressed billing items including IF billing, SmartNews charges, and Lively renewal. IAS Translation SOW scoped for upcoming work.

Contract Renewal

2025/2026 contract renewal discussions initiated October 3 and continued through December, ensuring partnership continuity and alignment on scope for the coming year.

Team Engagement

Weekly syncs maintained consistent team engagement through December 18. Resource allocation balanced across AnswerAI, Help Center/PRC, and security workstreams based on priority.

RISK MANAGEMENT

Risks & Blockers: Items Requiring Attention

Several risk areas and blockers emerged in Q4 that require proactive management and executive awareness to ensure smooth execution in Q1 2026.

Data Access Inconsistencies

Salesforce, Jira, and Confluence data access inconsistencies required debugging in November, revealing potential impact on AnswerAgent data quality. While resolved, ongoing monitoring is needed to prevent recurrence.

Contract Renewal Timeline

Contract renewal timeline needs finalization for continuity planning. Any delay could impact resource allocation and project momentum entering Q1 2026.

External Chatbot Dependency

External chatbot deployment is dependent on completing Fiddler Guardrails integration. This critical path item must be prioritized to meet customer-facing AI timelines.

Translation Automation SOW

Translation automation requires SOW finalization before development can begin. Delayed approval will push international content velocity improvements into later quarters.

Security Review Gates

Security review gates may extend deployment timelines. While necessary and appropriate, this requires planning buffer time into project schedules to avoid stakeholder expectation misalignment.

AAI Evaluation Results

AAI evaluation results are pending and may surface quality issues requiring remediation. Resource allocation flexibility needed to address findings quickly.

LOOKING AHEAD

Q1 2026 Roadmap: Strategic Priorities

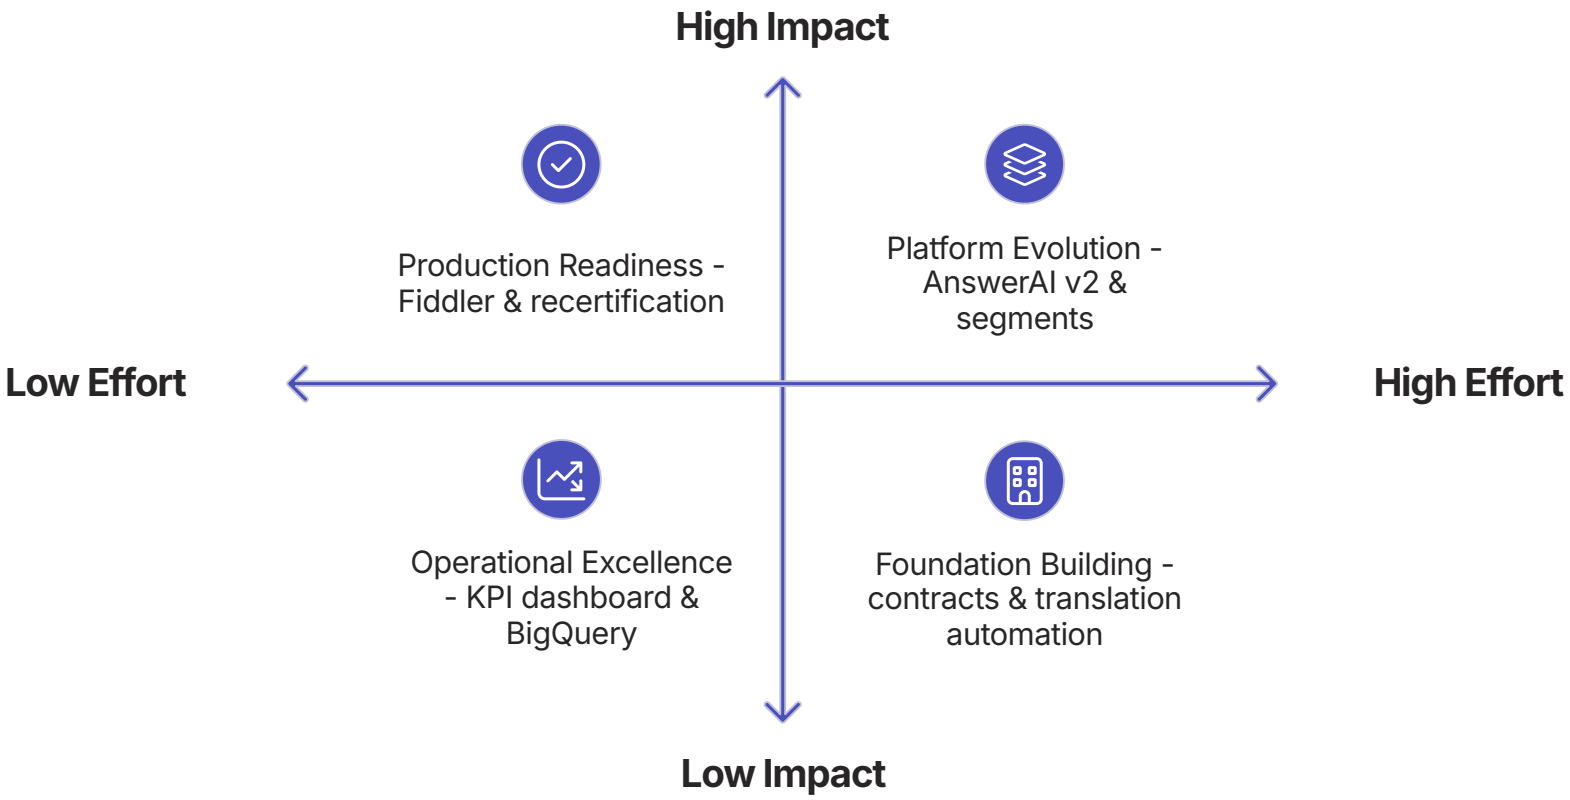

Q1 2026 priorities balance completing in-flight initiatives with advancing platform capabilities and operational maturity to support scale.

Q1 2026 Priorities: Detailed Roadmap

External Deployment Readiness

- Complete Fiddler Guardrails integration and deploy external chatbot with comprehensive safety measures
- Launch recertification flow to production following successful UAT completion
- Conduct final security reviews for customer-facing AI systems

Platform Advancement

- Advance AnswerAI v2.0 to release candidate status with RBAC and Workspaces functionality
- Implement Conveyor integration for PRC content surfacing in expanded contexts
- Expand Segment API integration capabilities based on user feedback

Content Operations

- Begin translation automation development based on finalized SOW
- Continue AAI evaluations and iterate on chatbot quality improvements
- Deepen BigQuery reporting automation for operational dashboards

Business Continuity

- Finalize 2025/2026 contract renewal to ensure seamless partnership transition
- Establish formalized KPI dashboard for executive reporting and visibility
- Plan Executive Strategic Alignment session for Q1 2026

PARTNERSHIP STRENGTH

Collaboration Highlights: Executive Alignment & Cadence

Strategic Alignment Sessions

Executive Strategic Alignment meetings held October 2 and November 20 provided leadership visibility into progress, risks, and strategic direction. These sessions ensured executive sponsorship remained strong throughout the quarter.

IAS Chief Sessions

IAS Chief sessions conducted through December 16 maintained hands-on engagement with internal AI chatbot users, gathering feedback and refining user experience based on real-world usage patterns.

Weekly Deployment Cadence

Weekly deployment sessions and syncs maintained throughout Q4 with consistent attendance and engagement, demonstrating operational discipline and commitment from both IAS and Last Rev teams to systematic progress.

This collaborative rhythm enabled rapid problem-solving, maintained alignment across workstreams, and built trust through consistent communication and delivery transparency.

Thank You & Next Steps

Thank you for your continued partnership and trust throughout Q4 2025. The progress achieved this quarter positions us well for successful external AI deployment, enhanced content operations, and platform maturity in 2026.

Immediate Action Items

01

Finalize contract renewal terms

Ensure partnership continuity into 2026

02

Complete UAT for recertification flow

Validate functionality before production launch

03

Progress Fiddler Guardrails to implementation

Critical path for external chatbot deployment

04

Review AAI evaluation results

Define improvement plan based on findings

05

Kick off translation automation SOW

Begin development on content velocity initiative

Looking Forward

Next Executive Strategic Alignment: TBD Q1 2026

Weekly syncs resume: January 2026

Contact: Last Rev Team

We look forward to continuing our collaboration and achieving the ambitious goals we've set for 2026 together.
